


| ID | Task Name | Duration | Predecessors | Feb 18, '07 | | | | | | |
|----|--|------------------|--------------|---|---|---|---|---|---|---|
| | | | | T | W | T | F | S | S | M |
| 1 | SBS Server Migration | 0 days | | 2/13 | | | | | | |
| 2 | Perform Hi-Level Site Assessment | 8 hrs | | CommNet Engineer, CommNet Account Executive | | | | | | |
| 3 | Preparation Work (Weekday Tasks) | 0.89 days | | | | | | | | |
| 4 | Prepare for Migration | 0.89 days | | | | | | | | |
| 5 | Collect information (7 Worksheets) | 4 hrs | | Customer, CommNet Engineer | | | | | | |
| 6 | Export Public Folders | 0.25 hrs | 5 | CommNet Engineer | | | | | | |
| 7 | Export Administrator Account Mailbox and Rules | 0.25 hrs | 6 | CommNet Engineer | | | | | | |
| 8 | Review Exchange mail quota (update?) | 0.1 hrs | 7 | Customer, CommNet Engineer | | | | | | |
| 9 | Communicate with users about project | 0.5 hrs | 8 | Customer | | | | | | |
| 10 | Request Users do "Clean Up" | 0.5 hrs | 9 | Customer | | | | | | |
| 11 | Ensure that Source Servers are Patch updated | 2 hrs | 8 | Customer | | | | | | |
| 12 | Stop Folder Redirection on Source Server | 0.5 hrs | 11 | CommNet Engineer | | | | | | |
| 13 | Ensure Source Servers are backed-up | 0.2 hrs | 11 | Customer | | | | | | |
| 14 | Ensure Users are logged off Heinkel Domain | 0.1 hrs | 9,13 | Customer | | | | | | |
| 15 | Perform Server Migration (Weekend Tasks) | 2.29 days | | | | | | | | |
| 16 | Configure replacement server (Part 1) | 0.93 days | 4 | | | | | | | |
| 17 | Install SBS 2003 on Server | 0.93 days | | | | | | | | |
| 18 | Disable DHCP Service on Source Server | 0 hrs | | 2/17 | | | | | | |
| 19 | Disconnect from Internet, Disable AV software | 0.1 hrs | 18 | CommNet Engineer | | | | | | |
| 20 | Connect Servers for the Migration | 0.1 hrs | 19 | CommNet Engineer | | | | | | |
| 21 | Install Destination Server | 1.5 hrs | 20 | CommNet Engineer | | | | | | |
| 22 | Complete Network Tasks | 1 hr | 21 | CommNet Engineer | | | | | | |
| 23 | Configure ISA Server | 0.75 hrs | 22 | CommNet Engineer | | | | | | |
| 24 | Configure Client Computers (Repoint Shortcuts) | 3 hrs | 23 | Customer | | | | | | |
| 25 | Prepare Client Computers for Account Migration | 1 hr | 24 | Customer | | | | | | |
| 26 | Begin the Migration | 1.6 days | 22 | | | | | | | |
| 27 | Install ADMT on Destination Server | 0.25 hrs | | CommNet Engineer | | | | | | |
| 28 | Create DNS Forwarders for Source & Destination Servers | 0.25 hrs | 27 | CommNet Engineer | | | | | | |
| 29 | Configure ADMT on the Destination Server | 0.25 hrs | 28 | CommNet Engineer | | | | | | |
| 30 | Migrate User Accounts | 0.25 hrs | 29 | CommNet Engineer | | | | | | |
| 31 | Migrate Group Accounts | 0.1 hrs | 30 | CommNet Engineer | | | | | | |
| 32 | Migrate Computer Accounts | 0.1 hrs | 31 | CommNet Engineer | | | | | | |

| | | | | | | |
|--|----------|--|-----------------|--|--------------------|--|
| Project: SBS Server Migration Date: Mon 9/17/07 | Task | | Milestone | | External Tasks | |
| | Split | | Summary | | External Milestone | |
| | Progress | | Project Summary | | Deadline | |

| ID | Task Name | Duration | Predecessors | Feb 18, '07 | | | | | | | | |
|----|---|------------------|--------------|-------------|---|---|---|---|---|---|---|--|
| | | | | T | W | T | F | S | S | M | T | |
| 33 | Move Exchange Mailboxes | 1.5 hrs | 32 | | | | | | | | | |
| 34 | Move Users and Other Shared Folders | 1 hr | 33 | | | | | | | | | |
| 35 | Configure the Destination Server (Part 2) | 0.96 days | 17,34 | | | | | | | | | |
| 36 | Assign Permissions to Migrated Accounts | 0.5 hrs | | | | | | | | | | |
| 37 | Assign Applications to Client Computers | 0.5 hrs | 36 | | | | | | | | | |
| 38 | Configure Printers & Faxes | 0.75 hrs | 37 | | | | | | | | | |
| 39 | Configure Backup Software (Exch., Sched.) | 4 hrs | 38 | | | | | | | | | |
| 40 | Configure Custom Settings (if any) | 0.1 hrs | 39 | | | | | | | | | |
| 41 | Start Folder Redirection | 0.1 hrs | 40 | | | | | | | | | |
| 42 | Configure Distribution Lists and Custom Recipient Polic | 0.5 hrs | 41 | | | | | | | | | |
| 43 | Enable Sending and Receiving eMails for migrated acc | 0.5 hrs | 42 | | | | | | | | | |
| 44 | Update Custom Logon Scripts | 0.5 hrs | 43 | | | | | | | | | |
| 45 | Add Users to the Remote Desktop Users Group | 0.25 hrs | 44 | | | | | | | | | |
| 46 | Disconnect Source Server from Network | 0.1 hrs | 35 | | | | | | | | | |
| 47 | Configure Heinkel Client Computers | 0.56 days | 30 | | | | | | | | | |
| 48 | Configure Clients with Windows 2000 or XP | 3 hrs | | | | | | | | | | |
| 49 | Configure Clients with Windows 95/98/ME/NT | 0 days | 48 | | | | | | | | | |
| 50 | Confirm Client PC Connectivity | 1.5 hrs | 49 | | | | | | | | | |
| 51 | Import Public Folders to Destination Server | 0.25 hrs | 46 | | | | | | | | | |
| 52 | Complete the Migration | 0.32 days | 26 | | | | | | | | | |
| 53 | Remove the DNS Forwarder for Source Server | 0.1 hrs | | | | | | | | | | |
| 54 | Remove Permissions granted for the Migration | 0.25 hrs | 53 | | | | | | | | | |
| 55 | Configure password Policies | 0.1 hrs | 54 | | | | | | | | | |
| 56 | Reconnect to the Internet | 0.1 hrs | 55 | | | | | | | | | |
| 57 | Recreate DNS Forwarders on Destination Server | 0.25 days | 56 | | | | | | | | | |
| 58 | Validate Server Migration Completed | 0.03 days | 52 | | | | | | | | | |
| 59 | Uninstall ADMT on the Destination Server | 0.25 hrs | | | | | | | | | | |
| 60 | Tasks for Monday following Migration | 0.38 days | 59 | | | | | | | | | |
| 61 | Resolve any outstanding issues | 3 hrs | | | | | | | | | | |
| 62 | Coordinate Migration of MAS-90 | 3 hrs | | | | | | | | | | |

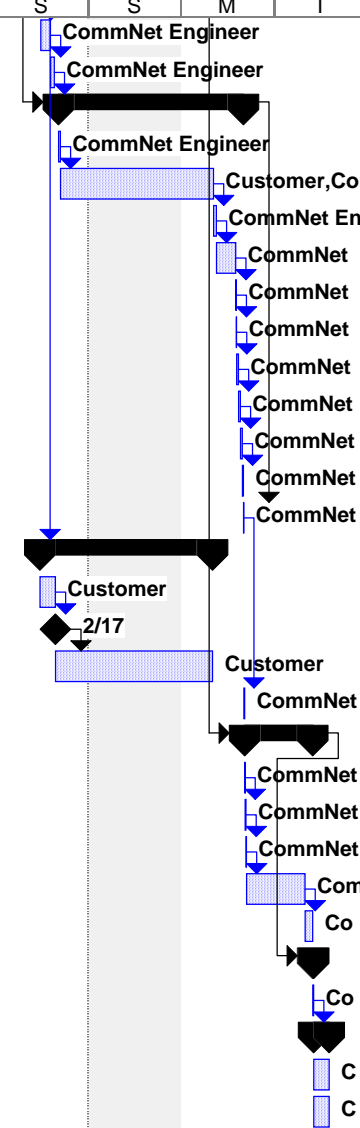

| | | | | | | |
|--|----------|--|-----------------|--|--------------------|--|
| Project: SBS Server Migration Date: Mon 9/17/07 | Task | | Milestone | | External Tasks | |
| | Split | | Summary | | External Milestone | |
| | Progress | | Project Summary | | Deadline | |
